Budget FY	Actual YTD	Committed	Forecast FY	EAC	Capex %	Projects to Review
54M	45.60M	7M	57M	56.80M	94.57%	2


programme

- [ ] Clearing
- [ ] Data and Reporting
- [ ] Infrastructure
- [ ] Regulatory
- [ ] Trading and Market Structure

entity

- [ ] LME
- [ ] LME Clear
- [ ] Shared

project_name	pm	Budget FY	Actual YTD	Variance %	Forecast FY	EAC Variance %	Forecast Change %	Variance Flag
Clearing Platform Replacement	Priya Nair	16,000,000	12,806,710.00	0.18%	16,068,000	0.42%	-0.71%	OK
Data Centre Migration	Rachel Chen	7,200,000	6,913,880.00	17.11%	8,442,000	17.05%	0.00%	Review
Electronic Trading Enhancements	Tom Hargreaves	7,000,000	5,774,020.00	-1.80%	6,980,000	-3.71%	0.52%	OK
Enterprise Data Platform	Sofia Meyer	4,000,000	3,211,140.00	-3.28%	5,600,000	40.00%	40.00%	Review
Management Reporting Automation	Sofia Meyer	2,000,000	1,691,880.00	-0.48%	1,985,000	-0.76%	-0.75%	OK
Margin and Collateral Upgrade	Priya Nair	4,000,000	3,283,180.00	-1.11%	3,980,000	-0.55%	0.76%	OK
Market Data Distribution Refresh	Tom Hargreaves	3,000,000	2,719,120.00	7.90%	2,897,000	4.54%	1.65%	OK
Network and Security Refresh	Marcus Webb	6,000,000	5,156,290.00	3.54%	5,986,000	2.24%	-1.14%	OK
Trade Reporting Controls	Daniel Okafor	1,800,000	1,535,890.00	-0.78%	1,785,000	-0.78%	-0.22%	OK
UK Regulatory Reporting Changes	Daniel Okafor	3,000,000	2,508,640.00	-2.77%	3,031,000	-1.85%	0.66%	OK
Total		**54,000,000**	**45,600,750.00**	**2.39%**	**56,754,000**	**5.18%**	**2.77%**	**Review**

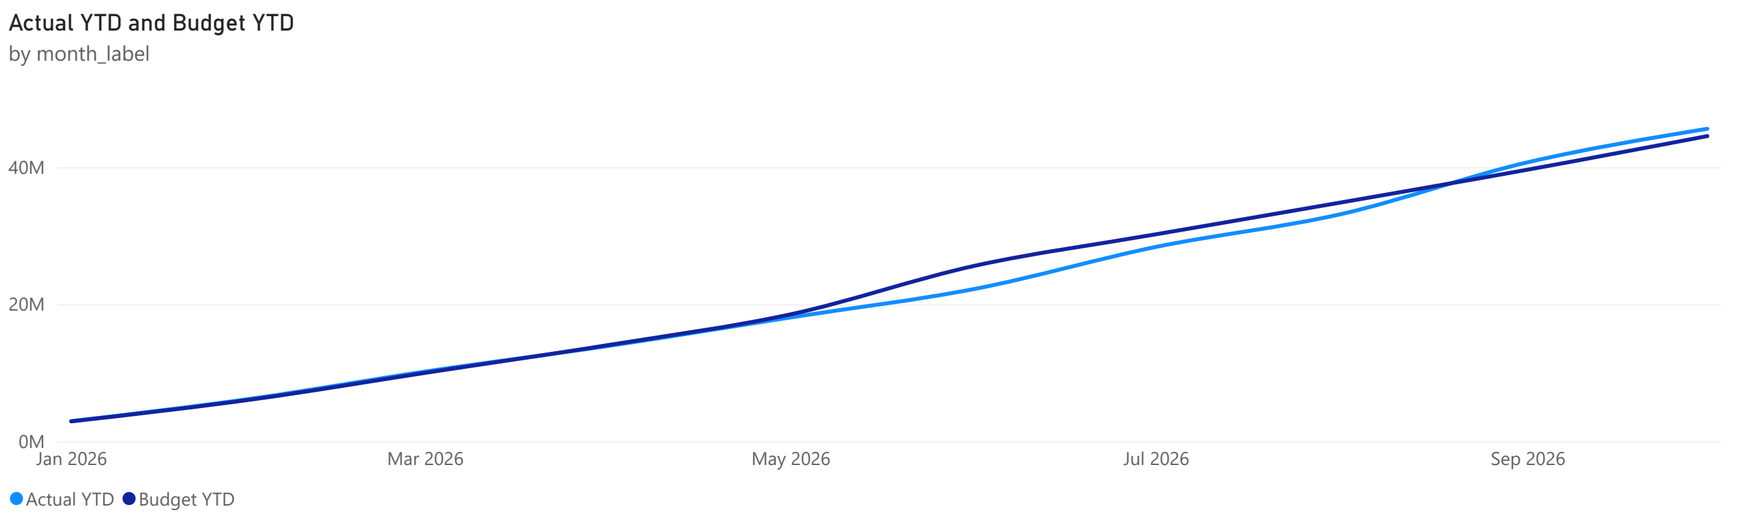


Synthetic project portfolio data. All names and figures are invented.

project_name

- [ ] Clearing Platform Replacement
- [ ] Data Centre Migration
- [ ] Electronic Trading Enhancements
- [ ] Enterprise Data Platform
- [ ] Management Reporting Automation
- [ ] Margin and Collateral Upgrade
- [ ] Market Data Distribution Refresh
- [ ] Network and Security Refresh
- [ ] Trade Reporting Controls
- [ ] UK Regulatory Reporting Changes

Forecast Bias %


by project_name

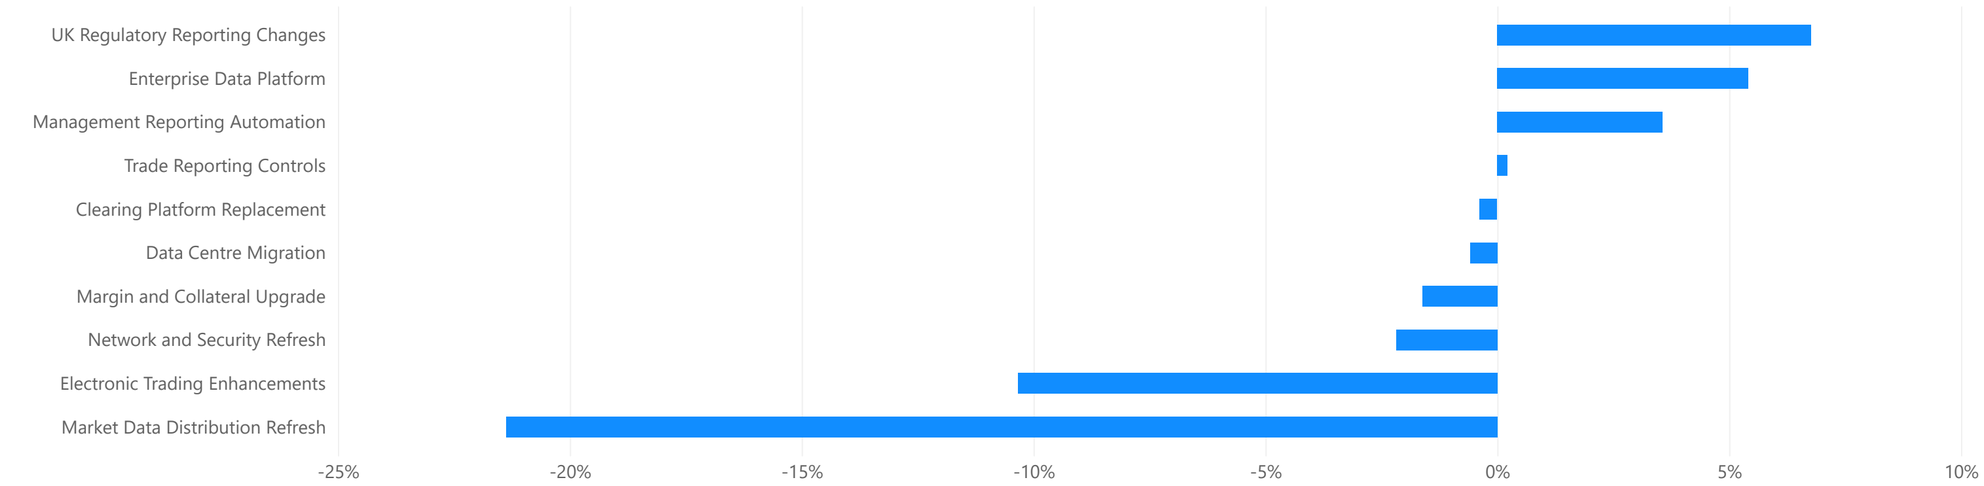

pm	Forecast Error %	Forecast Bias %
Daniel Okafor	6.01%	4.30%
Marcus Webb	5.73%	-2.18%
Priya Nair	2.60%	-0.62%
Rachel Chen	3.23%	-0.59%
Sofia Meyer	6.26%	4.78%
Tom Hargreaves	17.89%	-13.83%
Total	**6.54%**	**-2.23%**

Forecast FY Walk

by snapshot_month_end

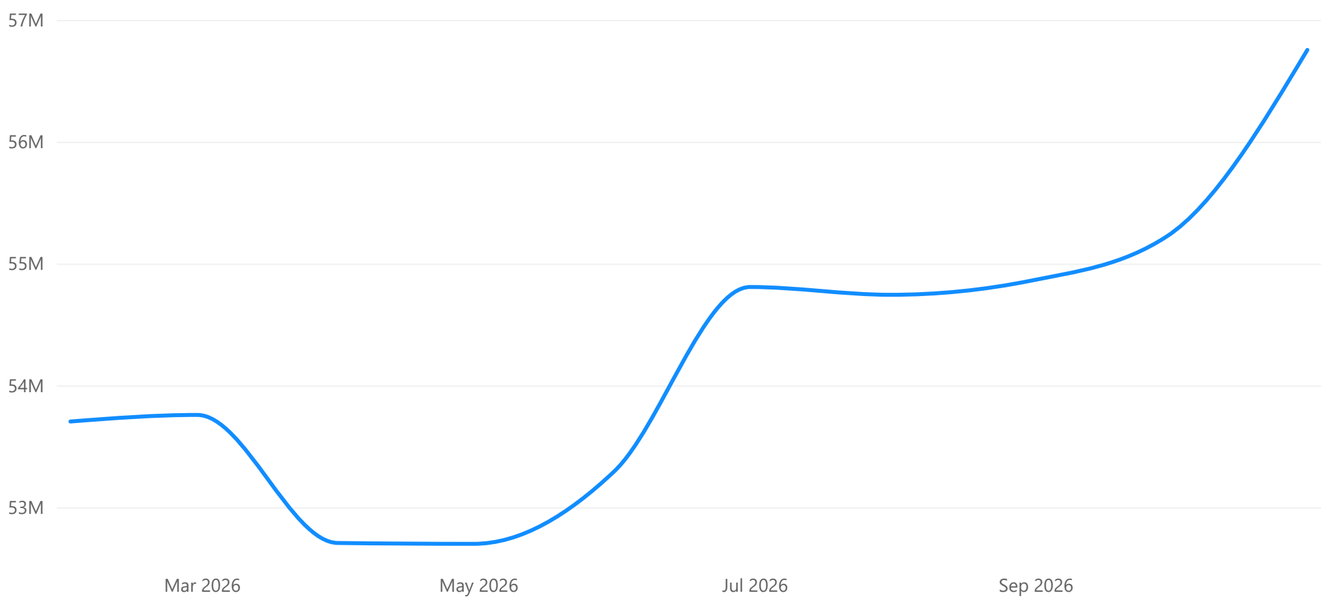

Synthetic project portfolio data. All names and figures are invented.

project_name

- [ ] Clearing Platform Replacement
- [ ] Data Centre Migration
- [ ] Electronic Trading Enhancements
- [ ] Enterprise Data Platform
- [ ] Management Reporting Automation
- [ ] Margin and Collateral Upgrade
- [ ] Market Data Distribution Refresh
- [ ] Network and Security Refresh
- [ ] Trade Reporting Controls
- [ ] UK Regulatory Reporting Changes

project_name	Actual YTD	Tracker Minus Ledger	Recon Status
Clearing Platform Replacement	12,806,710.00	290.00	OK
Data Centre Migration	6,913,880.00	-832,880.00	Not submitted
Electronic Trading Enhancements	5,774,020.00	239,980.00	Break
Enterprise Data Platform	3,211,140.00	-140.00	OK
Management Reporting Automation	1,691,880.00	120.00	OK
Margin and Collateral Upgrade	3,283,180.00	-180.00	OK
Market Data Distribution Refresh	2,719,120.00	-240,120.00	Break
Network and Security Refresh	5,156,290.00	-148,290.00	Break
Trade Reporting Controls	1,535,890.00	110.00	OK
UK Regulatory Reporting Changes	2,508,640.00	86,360.00	Break

invoice_ref	project_name	supplier	je_number	Sum of amount_gbp
INV-48213	Network and Security Refresh	Northfield Networks Ltd	JE-100590	148,500.00
INV-48213	Network and Security Refresh	Northfield Networks Ltd	JE-100591	148,500.00
Total				**297,000.00**

project_name	month_end	comment
Clearing Platform Replacement	30 June 2026	Catch-up accrual planned for July close
Data Centre Migration	30 June 2026	Hardware delivery ahead of plan
Network and Security Refresh	30 September 2026	Installation invoice received
Clearing Platform Replacement	31 May 2026	M4 licence milestone slipped to September; accruals pending
Clearing Platform Replacement	30 September 2026	M4 milestone paid
Enterprise Data Platform	31 July 2026	No change to forecast
Enterprise Data Platform	31 August 2026	No change to forecast
Enterprise Data Platform	30 September 2026	No change to forecast
UK Regulatory Reporting Changes	31 October 2026	October build invoice dated 29 October
Electronic Trading Enhancements	31 August 2026	Phase 2 delivery invoice received
Clearing Platform Replacement	31 July 2026	Q2 contractor accrual caught up
Clearing Platform Replacement	30 April 2026	Q2 contractor invoices not yet accrued
Data Centre Migration	30 September 2026	Racking and migration weekends over plan; forecast reflects run-rate
Enterprise Data Platform	31 October 2026	Vendor extension and licence true-up agreed; forecast updated

Synthetic project portfolio data. All names and figures are invented.
